



Woodrow  
Wilson  
Bridge  
Project

# Telegraph Road Interchange

## Project Update to the City of Alexandria Planning Commission

John D. Lynch, PE  
Jonathan A Jacobsen, PE

June 1, 2011



*Woodrow  
Wilson  
Bridge  
Project*

# Agenda

- **Project Scope & Current Status**
- **Schedule Status**
- **Long Term Impacts**
- **Short Term Impacts**
- **Goals for 2011**



Woodrow  
Wilson  
Bridge  
Project

# I-95 / Telegraph Rd Interchange






Woodrow  
Wilson  
Bridge  
Project

# Telegraph Road Interchange Improvements


I-95/Telegraph Road Interchange  
Overall Improvement

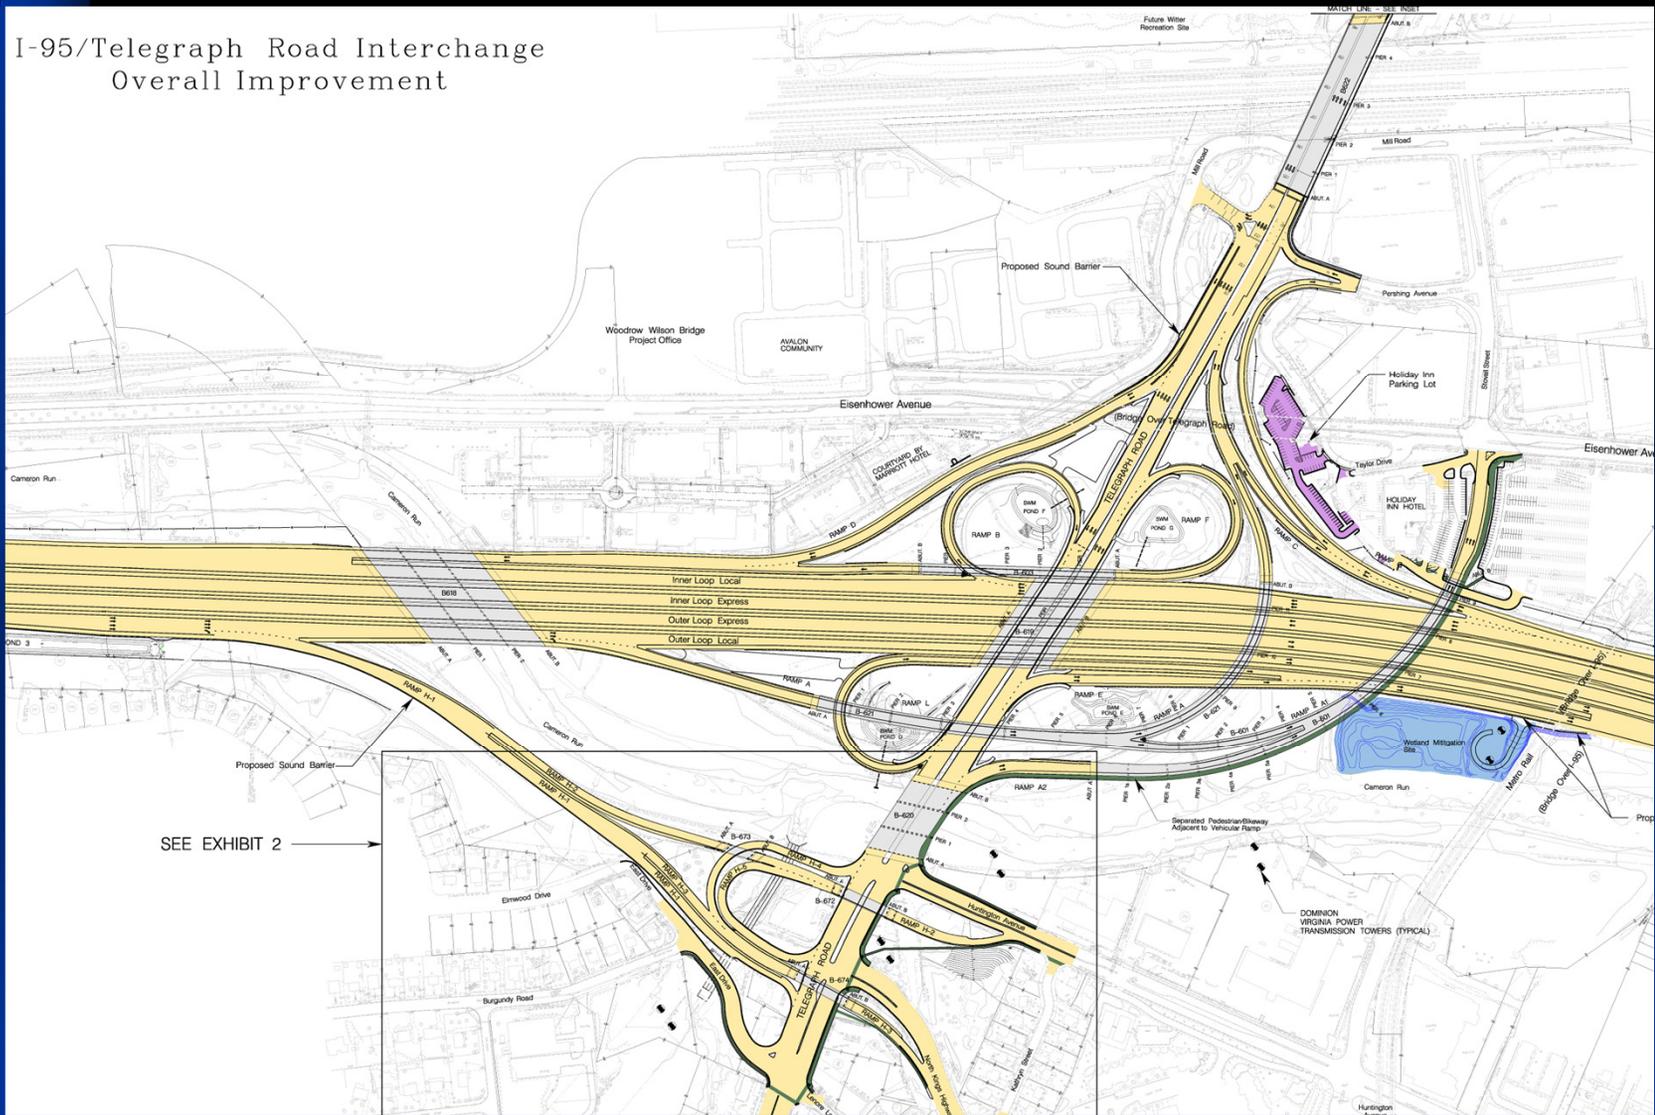



Woodrow  
Wilson  
Bridge  
Project

# Detail South of Beltway

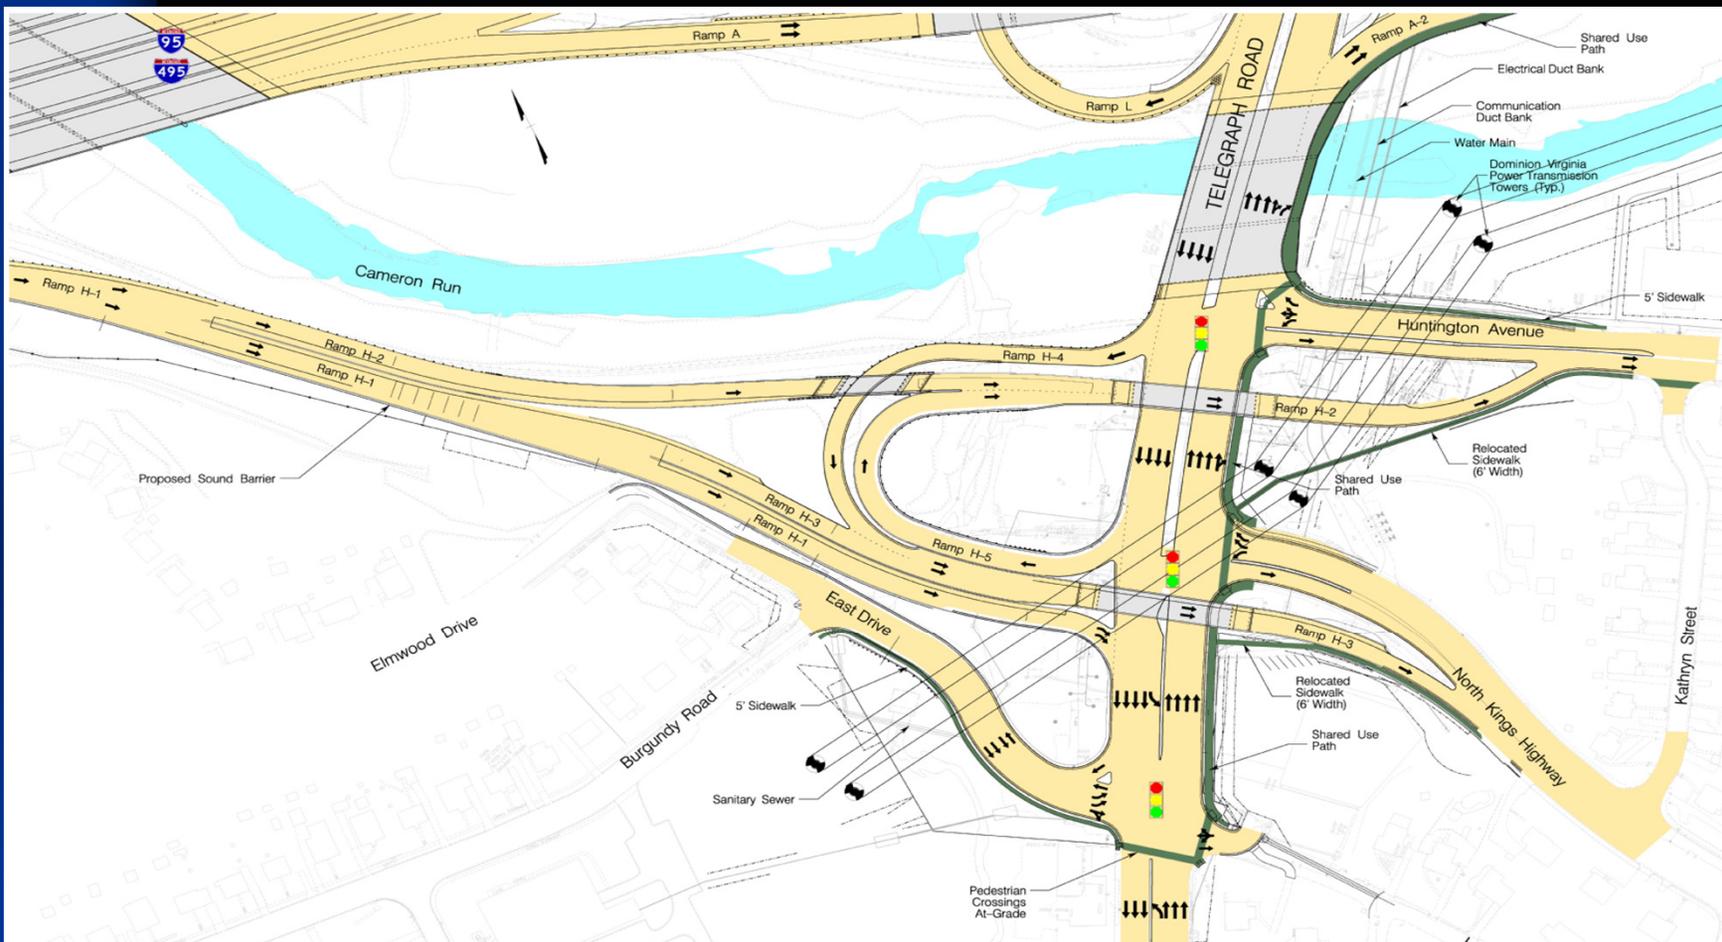






Woodrow  
Wilson  
Bridge  
Project

# As of February 23, 2011

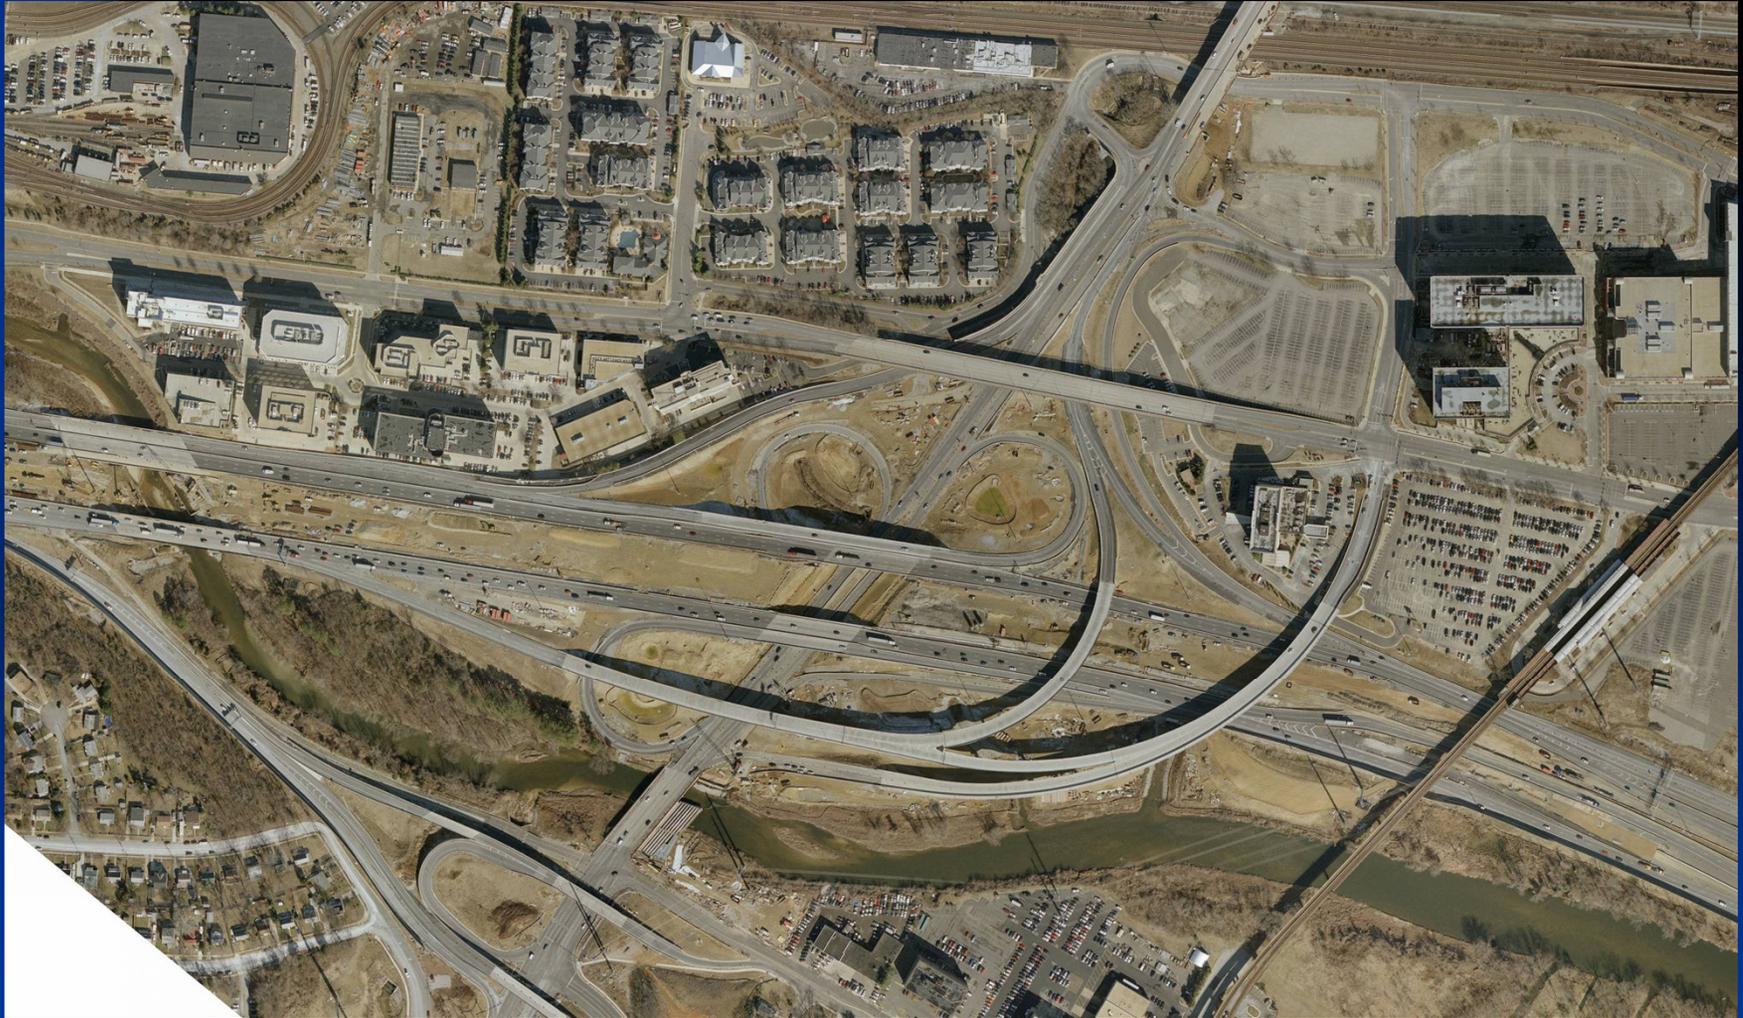



*Woodrow  
Wilson  
Bridge  
Project*

## Schedule Status

- **Work on final contract began February 2008**
- **75% work completed**
- **61% time completed**
- **Contract completion date: June 30, 2013**
- **On track for substantial completion late 2012**



*Woodrow  
Wilson  
Bridge  
Project*

## Long Term Impacts

- Beltway at three lanes, each loop, from Eisenhower Connector to east of Telegraph Rd
- Telegraph lanes restricted East Drive/Lenore Lane to Duke St
- Night and off peak day time lane and ramp closures



## Short Term Impacts

- **Telegraph closed N & S Duke St to Beltway**
  - Accommodates WMATA restrictions for bridge demo and construction
  - Weekends of June 3-5 and July 29-31
  - Two more weekends, in future
- **Westbound Pershing closed at Telegraph**
  - Construction of Pershing tie-in to widened Telegraph Rd bridge over railroads
  - July – September, 2011
  - Detour via Eisenhower and Holland Lane



Woodrow  
Wilson  
Bridge  
Project

## Goals for 2011

- Complete Express Lanes of Beltway
- Complete all Beltway ramps
- Complete first two of three stages of Telegraph Rd bridge over Cameron Run
- Complete first stage of Telegraph Rd bridge over railroads
